Strategic Initiatives Work Sample

Enterprise Governance, Portfolio Prioritization, and Executive Reporting

An anonymized example of governance design, cross-functional coordination, and portfolio decision support for a high-visibility, deadline-driven enterprise program.

Robert Frederick

Federal Science Agency • Program Management Office

Representative work product, anonymized for portfolio use

What This Sample Demonstrates

Overview

- Designed governance and prioritization structures for a multi-team portfolio operating under hard delivery deadlines and competing priorities.
- Created reporting, risk escalation, and workload visibility mechanisms to support leadership decision-making and execution discipline.
- Coordinated stakeholders across interconnected workstreams where success depended on shared timing, accountability, and early issue surfacing.
- Illustrates the kind of execution architecture I build to help complex organizations move from scattered effort to coordinated delivery.

About This Work Sample

Context, Role, and Leadership Contribution

Context

These materials were developed during a multi-year strategic delivery engagement at a federal science agency, supporting both a congressionally mandated publication program and a broader portfolio prioritization effort spanning multiple teams, dependencies, and hard delivery deadlines.

The publication program required coordination across 25+ internal stakeholders and contractors responsible for data readiness, table production, drafting, review, compliance, and outreach. In parallel, the prioritization framework provided leadership with a structured basis for sequencing competing releases across a shared production environment, replacing ad hoc decisions with a more transparent and repeatable governance approach.

25+

Coordinated Stakeholders
Program officers, data teams, contractors

2

Governance Frameworks Designed
Risk log, prioritization criteria, status reporting

7 yrs

Prior Delivery Failures Reversed
First on-time statutory release in 7 years

50+

Concurrent Projects Tracked
Via real-time dashboard and weekly status reviews

Role: Senior Manager (PMO) | Federal Science Agency | 2020 – 2024

SECTION 1 OF 2

Executive Reporting, Risk Management, and Stakeholder Coordination

Status reporting, risk management, and stakeholder coordination for a congressionally mandated federal publication.

Slides 4 – 6

Survey Data Availability — Task Status

Source data ingestion milestones across five survey programs

Tracks data handoff milestones from survey programs to the production data team. Status reflects schedule as of reporting date.

Survey Program	Status	% Complete	Milestone Date	Responsible Team	Notes
IPEDS Completions & Enrollments	**Completed**	**100%**	03/31/22	Data Lead	*Availability confirmed; tables in progress*
Survey of Earned Doctorates (SED)	**Completed**	**100%**	05/16/22	Survey Coordinator	*Availability confirmed; tables in progress*
National Survey of College Graduates (NSCG)	**Begin Planning**	**0%**	06/23/22	Survey Coordinator + Data Analyst	*Data team prep window: 6/23 – 7/21*
General Social Survey (GSS)	**Begin Planning**	**0%**	07/15/22	Survey Coordinator	*Milestone and data availability same date*
Survey of Doctorate Recipients (SDR)	**Begin Planning**	**0%**	07/08/22	Survey Coord + Data Analyst	*Data team prep window: 7/8 – 8/4; full avail 8/9*

Legend: Completed | In Progress | Begin Planning

Report Drafting Progress & Key Open Items

Active workstreams and pending decisions as of reporting date

DRAFTING & REVIEW STATUS

Workstream	Status	% Done	Target
Report Text & Figures (Part 1)	In Progress	86%	06/17/22
Writing Coach Review	In Progress	86%	06/17/22
Peer Review (Part 1)	Begin Planning	0%	06/20/22
Data Tables — IPEDS / SED	In Progress	40%	06/17/22
Data Tables — GSS / SDR / NSCG	Not Started	0%	07/26 – 08/15

KEY OPEN ITEMS

High

508 Compliance
Confirmation needed on handling approach given contractual constraints.

Active

Peer Review
Part 1 peer review to begin 06/20 — reviewer panel confirmed.

Medium

Social Media Outreach
Graph selection for social posts to be identified; outreach plan due early August.

Medium

FAQs / Microsite
"How Do I?" page converting to FAQ format; prior FAQ text to be pulled for reference.

Low

Report Naming
New report name under discussion with Leadership; follow-up pending.

Risk Register Summary

Active risks tracked in program risk log; linked to full SharePoint register

ACTIVE RISKS

R-01 | Medium Priority

Survey Data Timeline Compression

DESCRIPTION	MITIGATION	IMPACT
GSS 2021 and SDR 2021 data availability timelines create downstream pressure on report and data table review windows. Risk impact date: 7/29/22.	Coordination planning underway to sequence data intake into reporting workstreams; contingency review windows being established.	Schedule — late data delivery could compress peer review and compliance review windows by 2–3 weeks.

R-02 | Medium Priority

New Author Onboarding & Quality Risk

DESCRIPTION	MITIGATION	IMPACT
New staff brought on as report authors for the upcoming edition. Schedule adherence and deliverable quality require active monitoring.	Structured onboarding and training plan in place; writing coach review added as a quality gate.	Quality / Schedule — authoring delays or rework could cascade into peer review and finalization timelines.

Full risk log maintained in program SharePoint; risks reviewed at weekly status meeting and escalated to PMO leadership as warranted.

SECTION 2 OF 2

Portfolio Prioritization and Sequencing Framework

Criteria-based framework for sequencing competing releases across a multi-team production workload.

Slides 8 – 10

Prioritization Framework

Five-tier criteria system for production sequencing decisions

1	**Mandated Reports** ***Statutory requirement***	Reports required by federal law — highest scheduling priority, non-negotiable deadlines. Examples: Science & Engineering Indicators, WMPD.
2	**Data Releases** ***Primary data products***	InfoBriefs, Data Tables, InfoCharts, InfoBytes, and Public Use Files designated as the primary release for a given survey cycle.
3	**Non-Data Release (Topical)** ***Secondary topical products***	Topical InfoBriefs and Public Use Files not included in the primary data release. Includes standalone InfoBytes and InfoCharts.
4	**Non-Data Release (DST/DT)** ***Post-release data tables***	Detailed Statistical Tables or Data Tables released after the primary data release product has already been published.
5	**Working Papers** ***Research & analysis***	Working Papers developed by the Center or Program. Lowest scheduling priority relative to release-linked products.

Priority ratings applied by Production Team at intake; reviewed and adjusted based on schedule risk, workload, and dependency analysis.

Production Team Workload — Activities by Function

May through July 2022 | Based on scheduled activities across all active project schedules

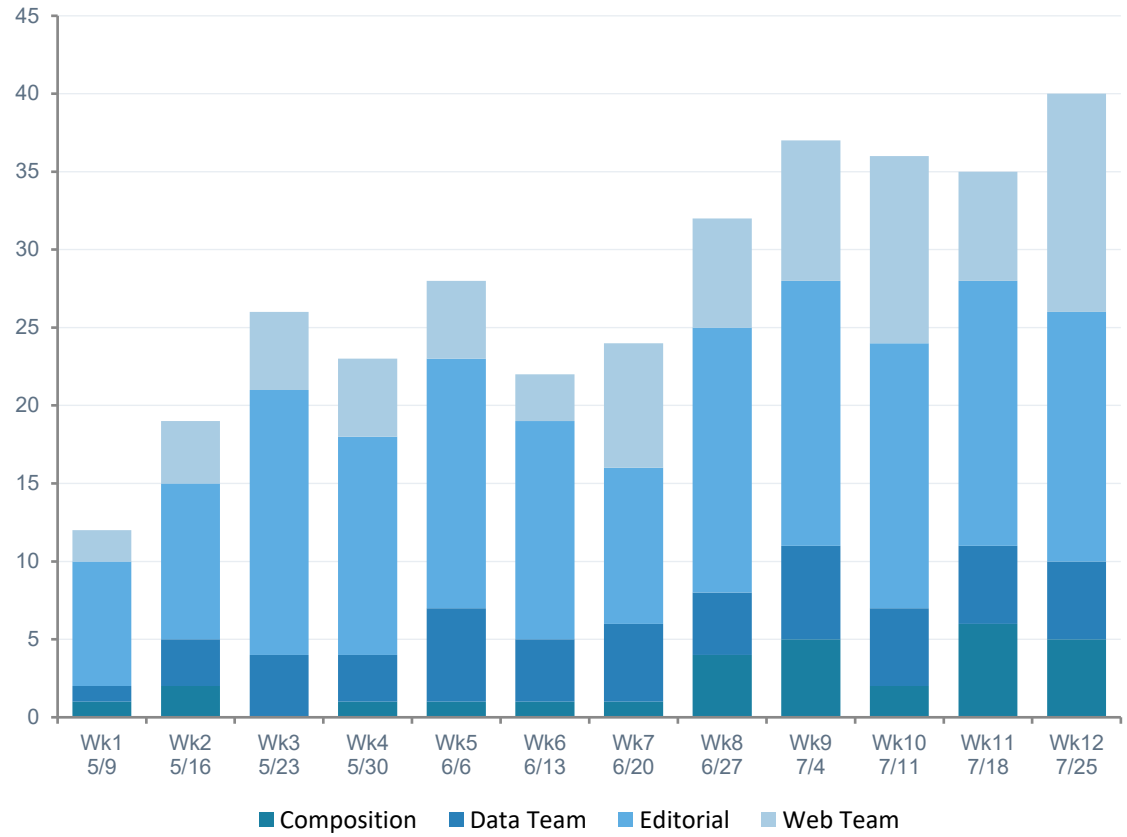

PEAK WEEK

Wk 11 (7/18)

35 total activities across all teams — highest single-week load in the planning window.

DOMINANT FUNCTION

Editorial

Editorial review accounts for ~54% of total scheduled activities throughout the window.

WEB TEAM SPIKE

Wk 12 (7/25)

Web team load triples from baseline by late July as releases approach publication deadlines.

PLANNING SIGNAL

Risk Window

Weeks 9–12 show compressing timelines across all four functions simultaneously.

Release Dependencies

Downstream scheduling constraints — initiatives and events driving sequencing decisions

The following products have hard dependencies on upstream releases, statutory mandates, or external events. Late delivery of prerequisite products creates cascading schedule risk.

Release / Deliverable	Prerequisite	Target Date	Dependency Type	Risk Level
2023 Flagship Report (WMPD)	GSS 2021, SDR 2021, NSCG 2021, SED 2021	**01/26/23**	**Statutory Mandate**	**High**
Science & Engineering Indicators	Multiple survey data releases (ABS, BERD, FFRDC)	Summer 2023	**Statutory Mandate**	**Medium**
GSS 2021 (Data Release)	Survey data availability (7/15/22)	10/31/22	Pre-req for WMPD	**Medium**
SDR 2021 (Data Release)	Survey data availability (7/8/22)	12/08/22	Pre-req for WMPD	**Medium**
SED 2021 Digest	SED Data Tables (released 10/07/22)	12/07/22	Pre-req for WMPD + external event	**Medium**
Council of College Graduates Mtg.	SED 2021 Digest, GSS 2021	**12/07/22**	External Event	**Medium**

Dependencies maintained in Production Prioritization tracker; reviewed weekly with Production Team leadership and updated as survey data availability milestones are confirmed.
